ID	Total Slack	Task Name	Duration	Start	Finish
1	0 days	MS Start project	0 days	2010-12-13	2010-12-13
2	0 wks	Inventarisation	1 wk	2010-12-13	2010-12-17
3	0 days	MS Kick off meeting	0 days	2010-12-17	2010-12-17
4	**0 days**	**Proposal A**	**15 days**	**2010-12-20**	**2011-01-07**
5	0 wks	A Developing proposal A	1 wk	2010-12-20	2010-12-24
6	2 days	A MS Issue proposal A for comments	0 days	2010-12-28	2010-12-28
7	0,4 wks	A Commenting period	1 wk	2010-12-29	2011-01-04
8	2 days	A Incorporate comments	3 days	2011-01-05	2011-01-07
9	2 days	A MS Issue updated proposal A	0 days	2011-01-07	2011-01-07
10	**0 days**	**Proposal B**	**17 days**	**2010-12-20**	**2011-01-11**
11	0 wks	B Developing proposal B	2 wks	2010-12-20	2010-12-31
12	0 days	B MS Issue proposal B for comments	0 days	2010-12-31	2010-12-31
13	0 wks	B Commenting period	1 wk	2011-01-03	2011-01-07
14	0 days	B Incorporate comments	2 days	2011-01-10	2011-01-11
15	0 days	B MS Issue updated proposal B	0 days	2011-01-11	2011-01-11
16	0 days	Kick off meeting evaluation process	0 days	2011-01-11	2011-01-11
17	0 wks	Evaluation proposal A & B	1 wk	2011-01-12	2011-01-18
18	0 days	MS Issue final evaluation report	0 days	2011-01-18	2011-01-18
19	0 days	MS Finish project	0 days	2011-01-18	2011-01-18

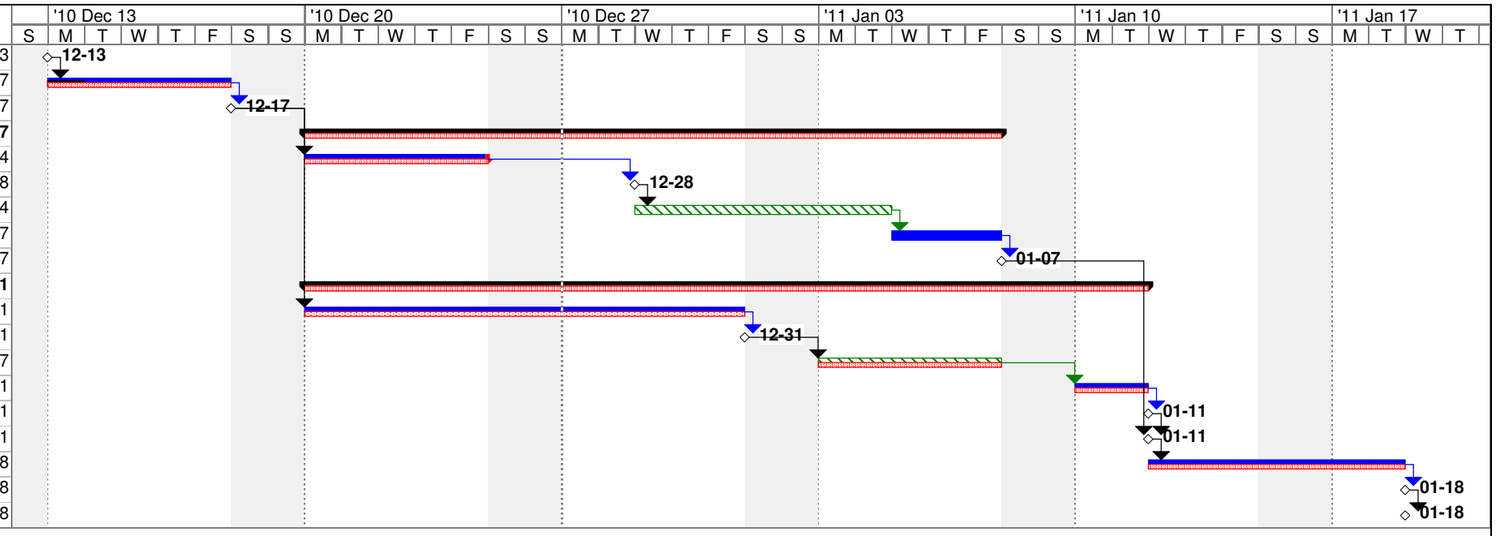

Project: Voorbeeld_10-12-13
Date: 2010-12-27

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone | Critical
